



# HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter


March 25, 2019 vol. 7

The HMII3 Project Team is managing the Historic Miramar Infrastructure Improvements Project Phase 3 (HMII3). The intent of this project is to update the 1950's era water mains and enhance fire protection. It will also provide sanitary sewer service that will allow property owners to abandon their septic tank once connected to the new sewer system, and improve storm water drainage in your neighborhood.

**We encourage you to contact the dedicated HMII3 customer service response team at [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz) or 954-998-3146 with questions or for additional information.**

## What's Taking Place in your Neighborhood?

- Roadway Restoration - *(Light Blue)* the construction of sidewalks, curbs, subgrade and base in preparation for the first lift of asphalt on SW 25<sup>th</sup> Street from SW 64<sup>th</sup> Avenue to SW 68<sup>th</sup> Avenue remains in progress.
- Roadway Restoration - *(Light Blue)* construction of curb, sub-grade and base on SW 20<sup>th</sup> Court going east is in progress.
- Roadway Restoration - *(Light Blue)* construction of curb, sub-grade and base are in progress on SW 20<sup>th</sup> Streets between SW 66<sup>th</sup> Avenue and SW 68<sup>th</sup> Avenue remains in progress.
- Sanitary Sewer - *(Green)* construction on SW 22<sup>nd</sup> Street and SW 22<sup>nd</sup> Court between SW 64<sup>th</sup> Avenue and SW 66<sup>th</sup> Avenue remains in progress. Construction on 67<sup>th</sup> Terrace between SW 67<sup>th</sup> Avenue and SW 66<sup>th</sup> Avenue remains in progress.
- Wellpoint Installation- *(Yellow)* is being installed on SW 24<sup>th</sup> Street at SW 64<sup>th</sup> Avenue going west to SW 66<sup>th</sup> Avenue and at SW 20<sup>th</sup> Court going north remains in progress.
- Watermain Construction *(Watermain)* are being installed along SW 67<sup>th</sup> Avenue.

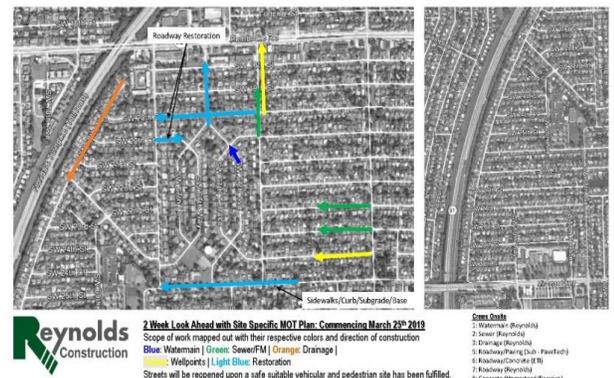

## What's Next?

- Roadway Restoration - *(Light Blue)* the first lift of asphalt on SW 25<sup>th</sup> Street is scheduled to be complete by the end of April 2019.
- Construction activity for new sanitary sewer pipe lines and water lines along Pembroke Road between SW 64<sup>th</sup> Avenue and SW 66<sup>th</sup> Avenue is scheduled to begin April 15, 2019.
- Storm drainage - *(Orange)* will be under construction on SW 21<sup>th</sup> and SW 22<sup>nd</sup> Streets from SW 66<sup>th</sup> Avenue to SW 64<sup>th</sup> Avenue.

**When Will It End? *HMII3 is scheduled for completion by September 2019.***
