



HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

September 16, 2019 Vol. 25

The HMII3 Project Team is managing the Historic Miramar Infrastructure Improvements Project Phase 3 (HMII3). The intent of this project is to update the 1950's era water mains, construct new storm drains and swales, and enhance fire protection with additional fire hydrants. It will also provide sanitary sewer services that will allow property owners to abandon their septic tanks once connected to the new sewer system, which will improve storm water drainage in your neighborhood.

Restoration of the first lift of asphalt on Pembroke Road from SW 67th Avenue to SW 64th Avenue continues. Restoration on Pembroke Road between SW 67th Avenue and SW 66th Avenue begins Sunday September 15, 2019 at 9:00 pm through September 18, 2019, weather permitting. To maintain the flow of traffic on Pembroke Road, the restoration construction schedule will consist of a one night shift from 9pm to 5am on Sunday, September 15 followed by two day shifts beginning on Monday, September 16, 2019 from 9am to 4pm for the rest of the week. The contractor, Reynolds Construction, Inc. will provide and maintain access to all driveways during restoration.

Did you know? As of September 13, 2019 the percentage of underground utilities that have been installed increased to 93%. The project date of completion is January 2020.

Reynolds Construction is now primarily focused on completing the construction of the storm drainage system and the various elements of restoration.

Stay current on HMII3 progress. The City of Miramar recently launched the HMII3 Interactive Map. The map allows you to follow the HMII3 construction activity in your area. The link below provides updates and progress status.

<https://www.miramarfl.gov/1621/HMII3-Interactive-Map>

For questions or concerns,
please contact 954.998.3146 or hmii3@adamsconsulting.biz
MIRAMARFL.gov | [@CityOfMiramar](https://twitter.com/CityOfMiramar)





HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

What's Taking Place in your Neighborhood?

- Roadway Restoration - (Light Blue) construction of asphalt driveways from SW 20th Street to SW 68th Terrace between Sunshine Boulevard to SW 68th Avenue remains in progress.
- Roadway Restoration - (Light Blue) Concrete driveways and sidewalks will be restored on SW 18th, SW 19th and SW 20th Streets between SW 68th Avenue and SW 66th Avenue Please do not park in your driveways remains in progress.
- Roadway Restoration - (Light Blue) roadway grading and paving on SW 67th Terrace from SW 21st Street to SW 23rd Street remains in progress. No parking on the roadway.
- Roadway Restoration - (Light Blue) roadway restoration on SW 23rd Street and SW 22nd Court from SW 66th Avenue to SW 64th Avenue remains in progress.
- Drainage Construction – (Orange) construction of new storm drains on SW 66th Avenue from SW 24th Street going north to SW 20th Street remains in progress.
- Drainage Construction – (Orange) construction of new storm drains from SW 67th Avenue from SW 20th Court to SW 20th Street remains in progress.
- Drainage Construction – (Orange) construction of new storm drains from SW 67th Terrace to SW 67th Lane remains in progress.
- Drainage and Sewer Construction – (Orange) construction of new storm drains on SW 18th Street and new sewer lines (Green) between SW 66th Avenue and SW 64th Avenue remain in progress.

We kindly request residents not to park on the roadway.


Please follow traffic signs and drive slowly.

For questions or concerns,
please contact 954.998.3146 or hmii3@adamsconsulting.biz
MIRAMARFL.gov | [@CityOfMiramar](https://twitter.com/CityOfMiramar)





HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

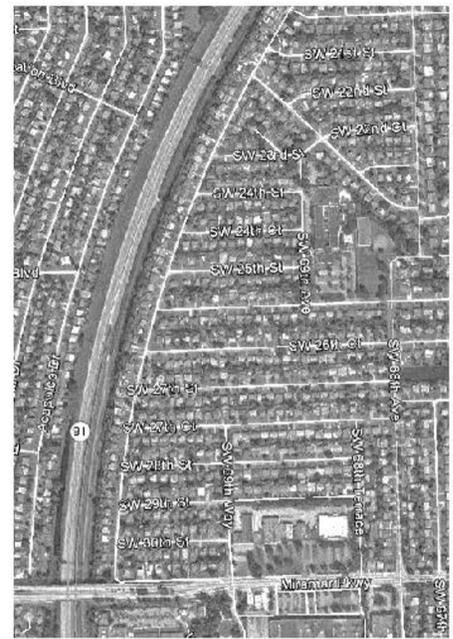

2 Week Look Ahead with Site Specific MOT Plan: Commencing September 16th 2019

Scope of work mapped out with their respective colors and direction of construction

Blue: Watermain | **Green:** Sewer/FM | **Orange:** Drainage | **Light Blue:** Restoration

Streets will be reopened upon a safe suitable vehicular and pedestrian site has been fulfilled.

Crews Onsite

- 1: Watermain (Reynolds)
- 2: Sewer (Reynolds)
- 3: Drainage (Reynolds)
- 5: Roadway/Paving (Subcontractor)
- 6: Roadway/Concrete (Subcontractor)
- 7: Roadway (Reynolds)
- 8: Concrete (Subcontractor)
- 9: Sodding (Subcontractor)

For questions or concerns,
please contact 954.998.3146 or hmii3@adamsconsulting.biz
MIRAMARFL.gov | [@CityOfMiramar](https://twitter.com/CityOfMiramar)

