



**YOU ARE INVITED**  
to the  
**HMI13 COMMUNITY MEETING**  
at the  
**MIRAMAR MULTI-SERVICE COMPLEX**  
on **AUGUST 14, 2019** at **7PM**

**LEARN ABOUT PROJECT UPDATES**

**MEET PROJECT TEAM MEMBERS**

**WEDNESDAY, AUGUST 14, 2019**  
**AT 7:00PM**  
**MIRAMAR MULTI-SERVICE COMPLEX**  
**6700 MIRAMAR PARKWAY**  
**MIRAMAR, FL 33023**

**FOR MORE INFORMATION**  
**PLEASE CONTACT THE HMI13**  
**CUSTOMER SERVICE TEAM**  
**AT 954.998.3146**



# HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

July 29, 2019 Vol. 19


The HMII3 Project Team is managing the Historic Miramar Infrastructure Improvements Project Phase 3 (HMII3). The intent of this project is to update the 1950's era water mains and enhance fire protection. It will provide sanitary sewer services that will allow property owners to abandon their septic tanks once connected to the new sewer system, which will improve storm water drainage in your neighborhood.

The HMII3 overall percentage of completion has increased by 4% to an overall 89% as of July 24, 2019. Reynolds Construction is focusing attention to roadway restoration, and testing the new systems in a phased approach. Restoration is focused on the light blue areas of the map. The project is scheduled for completion December 2019.

We encourage you to contact the dedicated HMII3 customer service response team at [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz) or 954-998-3146 with questions or for additional information.

## What's Taking Place in your Neighborhood?

- Roadway Restoration - (Light Blue) construction of roadway grading and curbing on SW 67th Terrace from SW 21st Street to SW 23rd Street remains in progress. Please follow traffic signs and drive slowly.
- Roadway Restoration - (Light Blue) construction of roadway grading and curbing on SW 67th Avenue from SW 21st Street to SW 23rd Street remains in progress. Please follow traffic signs and drive slowly.
- Roadway Restoration - (Light Blue) roadway grading on Sunshine Boulevard/SW 68th Way between the cul-de-sac (dead end) and SW 68th Terrace remains in progress. No parking on the roadway. Please drive slowly and follow traffic signs.

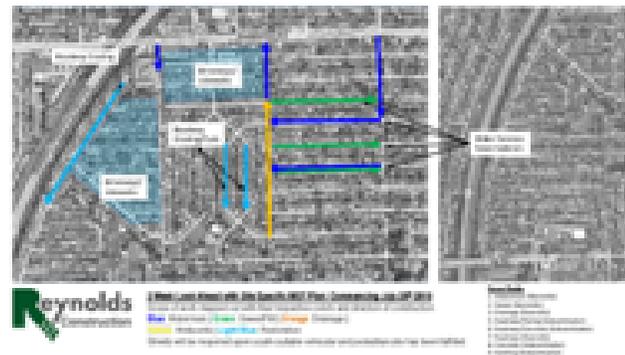

For questions or concerns,  
please contact 954.998.3416 or [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz)  
[MIRAMARFL.gov](http://MIRAMARFL.gov) | @CityOfMiramar

it's  
**RIGHT  
HERE**  
in MIRAMAR...



# HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

- **Roadway Restoration-** (Light Blue) construction of the driveways and sidewalks between SW 68th Avenue and Sunshine Boulevard from SW 19th Street to SW 67th Terrace remains in progress. Reynolds Construction has completed constructing asphalt driveways, paved concrete driveways and stamped concrete driveways will follow.
- **Dewatering** remains in progress, and is required until testing is completed. The dewatering equipment is required along SW 25th Street. Weather permitting, testing is expected until September 1, 2019.
- **Sanitary Sewer -** (Green) laterals lines are being installed along SW 20th Court and SW 21st Street between SW 64th Avenue to SW 66th Avenue, remains in progress. No parking on curbsides.
- **Water main Construction -** (Dark Blue) construction of the water main line and installation of sanitary sewer laterals - (Green) along SW 22nd Street between SW 64th Avenue to SW 66th Avenue remains in progress. No parking on curbsides.
- **Water main Construction -** (Dark Blue) water main line construction on SW 64th Avenue from Pembroke Road going south to SW 20th Court remains in progress.
- **Water main Construction -** (Dark Blue) water main line construction on SW 66th Avenue northbound from SW 22nd Street to Pembroke Road remains in progress.
- **Drainage Construction –** (Orange) construction of new storm drains on SW 66th Avenue from SW 24th Street going north to SW 20th Street remains in progress. Drive slowly, expect delays and follow traffic signs.

For questions or concerns,  
please contact 954.998.3416 or [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz)  
[MIRAMARFL.gov](http://MIRAMARFL.gov) | [@CityOfMiramar](https://twitter.com/CityOfMiramar)

it's  
**RIGHT  
HERE**  
in MIRAMAR...



# HISTORIC MIRAMAR INFRASTRUCTURE IMPROVEMENTS PROJECT (HMII3) Newsletter

## Pembroke Road Business Area – Remains In Progress

- Water main Construction and sewer line construction on Pembroke Road beginning at SW 68th Street going east to SW 64th Avenue is now complete. The water line construction at Pembroke Road the intersections of SW 68th Avenue, SW 66th Avenue and SW 64th Avenue remains in progress.
- There will be no parking in front of SW 6400 Pembroke Road from Monday July 29, 2019 to Wednesday July 31, 2019 due to roadway restoration. Customers are asked to park in the rear parking lot.

Construction is scheduled from 7 am to 4 pm Monday through Friday and from 9 pm to 5 am Sunday through Thursday.

Expect delays.

Weather permitting, the projected end date for this segment of the project is July 31, 2019.

What's Next?

HMII3 Community Meeting  
Wednesday, August 14, 2019 at 7pm  
Miramar Multi-Service Center  
6700 Miramar Parkway, Miramar, FL

If you have reported damages to your sprinkler system, driveway or other damages as a result of HMII3 construction, the damages will be repaired by Reynolds Construction. Please contact 954-998-3146 or [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz) to report damages.

For questions or concerns,  
please contact 954.998.3416 or [hmii3@adamsconsulting.biz](mailto:hmii3@adamsconsulting.biz)  
[MIRAMARFL.gov](http://MIRAMARFL.gov) | [@CityOfMiramar](https://twitter.com/CityOfMiramar)

